
Commercial Laboratory Project 9

1/2 EMT Conduit Assignment

(90 Degree Back-to-Back)

- 1. Make each conduit bend from the measurements provided.
- 2. Conduit ends must be reamed to remove sharp edges.
- 3. Offsets are required at all box locations.
- 4. All measurements must be within 1/8 inch of specified design.
- 5. All fittings must be secure at box location.
- 6. Work must in accordance with the National Electrical Code.
- 7. Label conduit with your name and submit to Instructor.

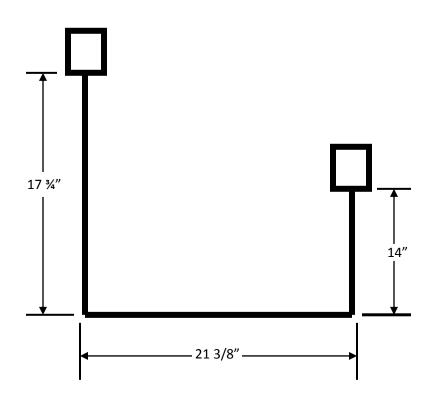

NAME: ______, Date: ______.

Points Received: ______, Instructor's Initials: ______.

Instructor's Remarks:
